

Motion Capture Lab

Update:

The project is now complete and in use.

Final built out being completed.



The structure I-Beams are being installed and the building will be arriving shortly.


January 28, 2016



January 13, 2016

Crews have completed the electrical service to the building and the foundation is ready for the arrival of the building scheduled the week of January 19, 2016. Once the building is in place, build-out of the interior will begin with completion by the end of February 2016.

This 1,920 square foot structure, located adjacent to the Kokernot Outdoor Theater is intended as a classroom and laboratory production space to expand curriculum and increase student enrollment for motion capture and video production classes as listed in the CSAT degree plan. Motion Capture, Basic Video Production, Advanced Video Production, Basic Audio Production, Advanced Audio Production, and Acting for Animators will all use this space. A contract is in place with Noble General Contractor (El Paso). Classes are scheduled in the facility for the 2016 Spring semester.

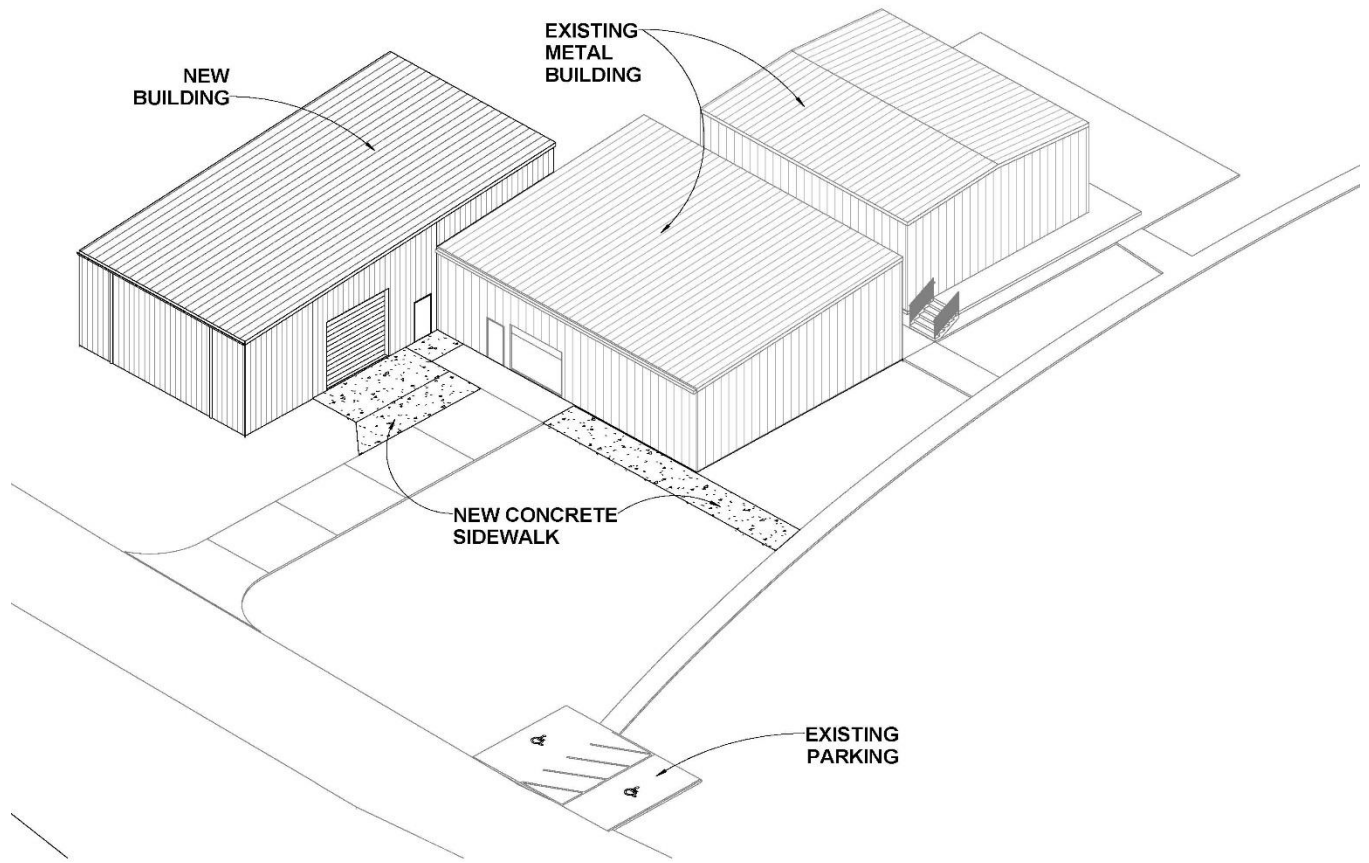

3-D Site Plan – PBK Architects
Site preparation underway. (10-26-15)



Site preparations continue (11-04-15)



Foundation poured (11-13-15)

